USER GUIDE

Eurolux Doors and Windows Installation Planner

A practical, step-by-step guide to scheduling projects, allocating teams, tracking WA production, and running the daily factory schedule.

Prepared for Eurolux office staff

Covers: Schedule · Team Allocation · Dashboard · WA Tracker · Daily Schedule

Updated edition — reflects the redesigned Schedule tab: Show/Hide Columns, repositioned Pending actions, Normal/Compact view, Project status, and the single shared search field.

Contents

1. **Getting started**
   Opening the app, the toolbar, and what "Synced with team" means

2. **The Schedule tab**
   Your project list — fields, Pending actions, hide/unhide, Show/Hide Columns, Compact view, Project status

3. **The Schedule grid**
   The day-by-day calendar view of every project's install window

4. **The Team Allocation tab**
   Who's doing what, when — a month-by-month view by team

5. **The Dashboard tab**
   KPIs, charts, reports, and clearing the schedule

6. **The WA Tracker tab**
   Tracking glass, frame and coating production for every job

7. **Sharing the WA Tracker with the factory**
   Giving the factory a tracker-only link

8. **The Daily Schedule tab**
   Today's team assignments, replacing the WhatsApp message

9. **How the installation process maps to the app**
   Suppliers, delivery timelines, NOC/access pass, payment gating, snagging and handover

10. **Tips, safety nets and troubleshooting**
    Undo, Clear all, installing the app, per-device settings, and where the data lives

CHAPTER 1

Getting started

The Installation Planner is a single web app with five tabs across the top: **Schedule**, **Team Allocation**, **Dashboard**, **WA Tracker**, and **Daily Schedule**. Every tab shares the same toolbar — though, as of this edition, a few toolbar controls only appear on the tab(s) that actually use them (see below) — and, if your office has shared sync turned on, the same live data, so everyone who opens the app sees the same thing, updated within a second of any change.

Switching tabs

Click **Schedule**, **Team Allocation**, **Dashboard**, **WA Tracker**, or **Daily Schedule** in the toolbar to switch views. Nothing is lost when you switch away from a tab — come back to it any time and your place, filters, and unsaved typing are exactly as you left them.

> **New:** the toolbar now shows only what each tab needs. **Show/Hide Columns**, **Reset columns**, **Show hidden rows**, and **Compact view** only appear on the Schedule tab, since they only affect that screen. There is also now just **one search field** in the whole app — it filters whichever tab you're currently on (Schedule or WA Tracker), and disappears on tabs that don't search anything, like the Dashboard.

Is my data shared with the rest of the office?

Look at the small badge in the toolbar, next to **Date filter**:


- **Synced with team** (green dot) — you're connected to the shared backend. Every edit you make is visible to everyone else using the planner within a second, and vice versa.
- **Saved on this device only** (grey dot) — the shared backend isn't reachable right now, so your changes are saved to this one browser only. Nothing is lost, but no one else will see it until shared sync is working again.

Click **Sync now** at any time to retry the connection without reloading the page — handy right after fixing a network issue.

CHAPTER 2

The Schedule tab

This is your project list — one row per project, scrolling sideways through every field. The screenshot below shows the current column order, with one column (Client) hidden to demonstrate **Show/Hide Columns**.

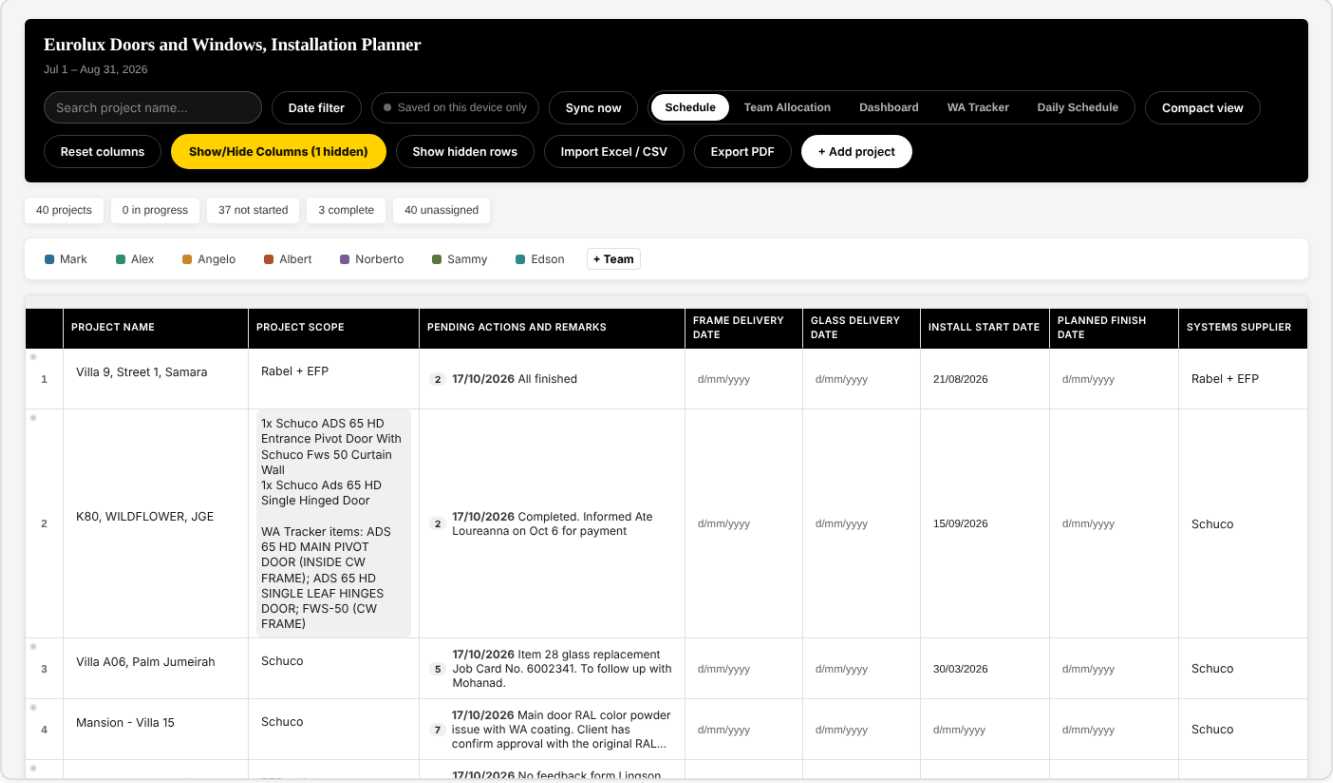

The Schedule tab — Client hidden, Show/Hide Columns highlighted yellow with a count, team roster includes Norberto.


Field order, left to right

#	Field	Notes
1	Project name	Can't be hidden.
2	Client	
3	Project scope	For SCHUCO jobs, matching WA Tracker line-items are appended automatically.
4	**Pending actions and remarks**	Moved right after Project scope in this edition — see below.
5	Frame delivery date	No restriction — any date.
6	Glass delivery date	No restriction — any date.
7	Install Start Date	
8	Planned Finish Date	
9	Systems supplier	
10	% complete	
11	Assigned team	Mark, Alex, Angelo, Albert, Norberto, Sammy, Edson, or a new one you add.
12	Helper teams	Any number of additional teams helping on the same job.
13	RAL / Glass	

14	Project value (AED)	
15	Design approval date	
16	Bonding required	Yes/No.
17	**Project status**	New in this edition — see below.

Pending actions and remarks

A dated, multi-entry log per project — click the cell (it shows the most recent entry and a count badge) to open a small modal, add a new dated note any time, or delete an old one. It now sits right after **Project scope**, since it's usually the first thing you want to check on a project.

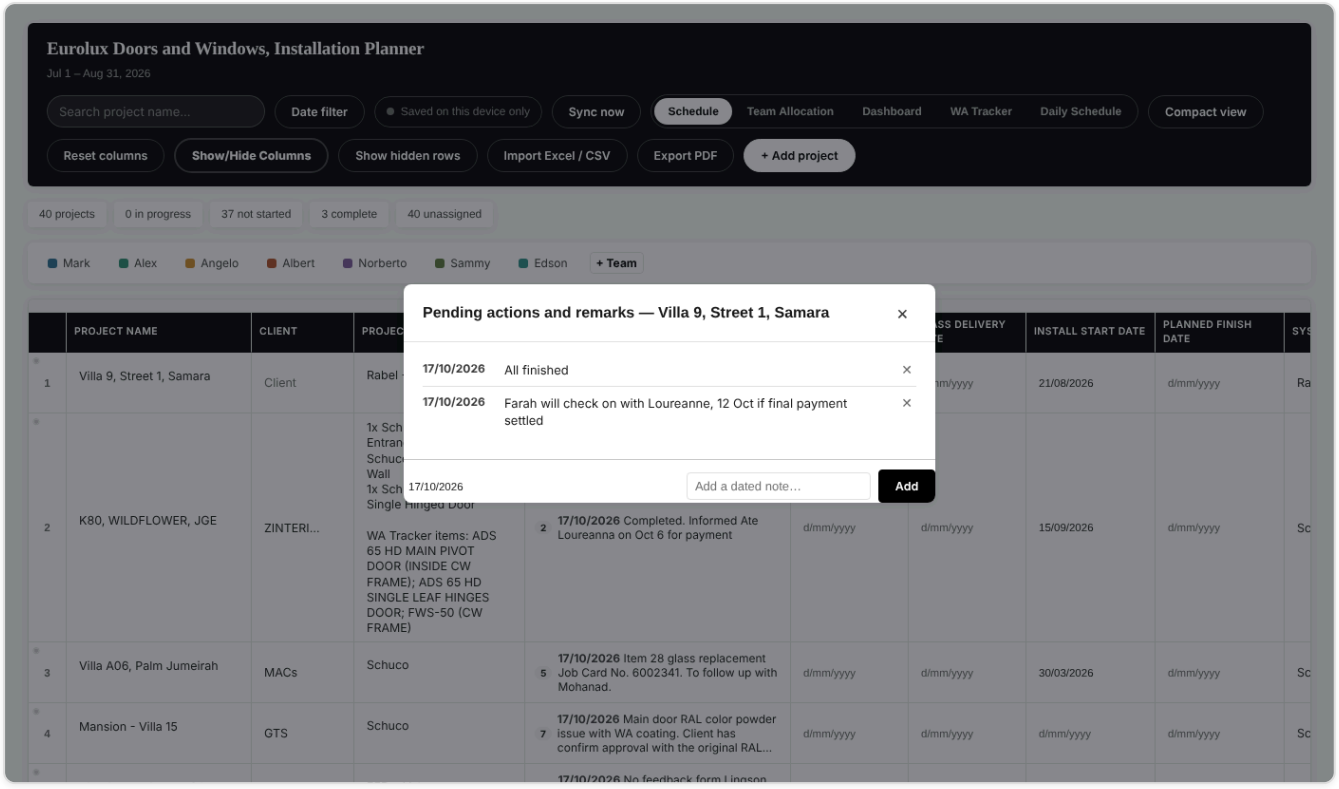

The Pending actions and remarks modal.

Show/Hide Columns

Click **Show/Hide Columns** in the toolbar to open a checklist of every column (except Project name, which can't be hidden). Untick any you don't need right now and it collapses away cleanly; tick it again to bring it back. The button itself turns **yellow** and shows a count — e.g. *"Show/Hide Columns (2 hidden)"* — any time one or more columns are currently hidden, so it's obvious at a glance that the grid isn't showing everything. **Reset columns** puts both widths and hidden columns back to the defaults. This preference, and column widths, are per-device (not synced) — hiding a column on the office computer doesn't hide it on someone else's screen.


Hide/unhide rows

Click the small ● next to a project's row number to hide that project from the plain Schedule list. **Show hidden rows** in the toolbar brings hidden rows back into view, dimmed, so you can still edit or unhide them. A hidden project is only ever hidden from the plain Schedule list — it still counts normally in the Dashboard's KPIs and charts, the Schedule grid popup, and Team Allocation.

Normal view / Compact view

The new **Compact view** button (next to Show/Hide Columns) tightens row height and field padding so more projects fit on screen at once — click it again (now labelled **Normal view**) to switch back. This is

remembered per device, the same way column widths are.

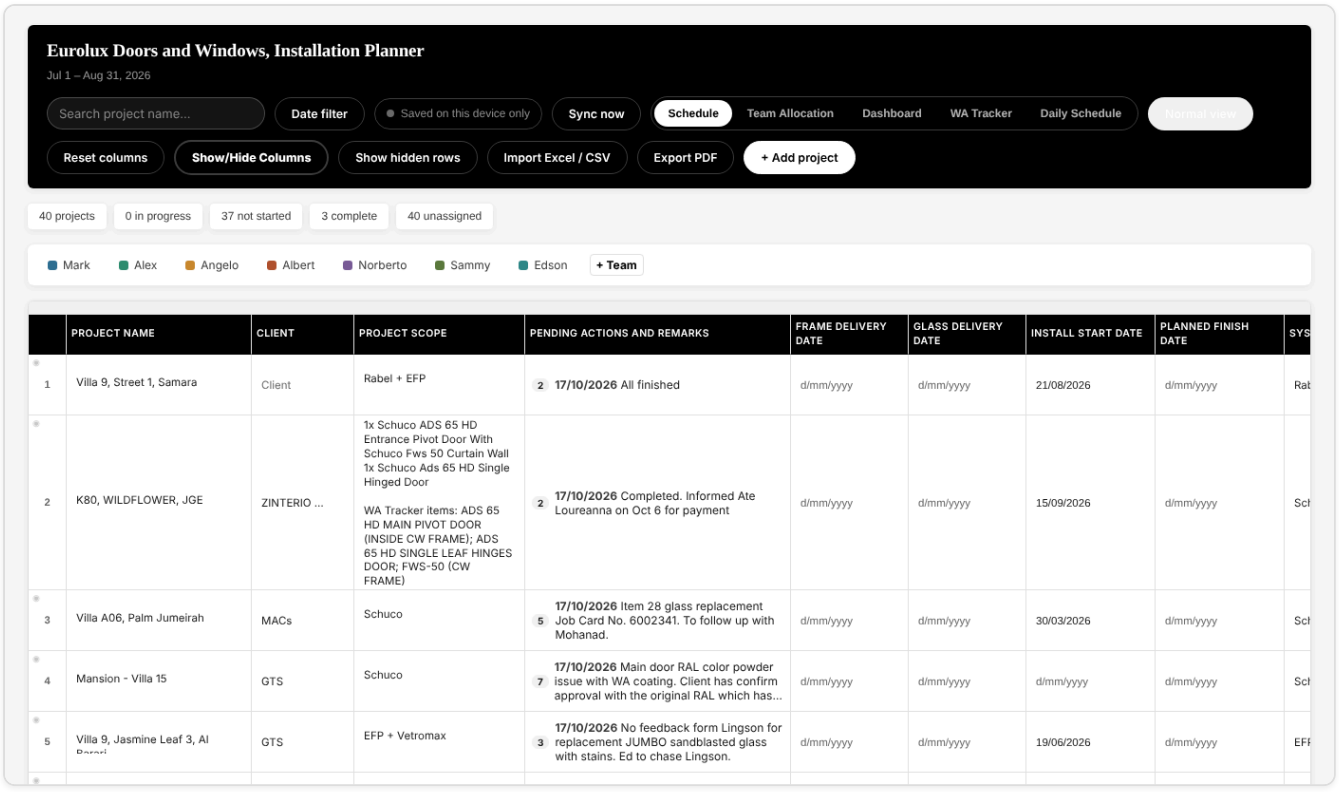

The same list in Compact view — more rows visible without scrolling.

Project status

A new dropdown with the project's current stage: **Installation in progress**, **Completed**, **Snagging in progress**, **Snagging completed**, **Awaiting handover to client**, or **Handed over**. If none of those fit, choose **Other...** and a free-text box appears to describe it in your own words.

Searching and filtering

Type into the single search box in the toolbar to filter the list to projects whose name matches. Click a team name in the legend, or a "not started / in progress / complete / unassigned" pill in the stats row, to show only matching projects; click again (or "clear ×") to reset.

Importing and exporting

Import Excel / CSV recognizes common header names (Project Name, Client, Scope, Systems Supplier, Frame/Glass Delivery Date, Install Start Date, Planned Finish Date, % Complete, Assigned Team, Helper Teams, RAL/Glass, Project Value, Design Approval Date, Bonding Required, Project Status, and Pending Status/Installation Pending/Remark) in any order. **Export PDF** exports a summary table of whatever is currently visible (respects an active filter).

CHAPTER 3


The Schedule grid

The day-by-day Gantt view — each project's install window shown as a colored bar on a calendar — lives separately from the main list. Open it from the **View schedule grid** button at the top of the Dashboard tab; it opens in a large popup with its own Compact view toggle, and closes with the × button, Esc, or a click outside it. The calendar starts 1 July 2026 and stretches forward automatically to cover whatever project has the latest finish date.

The grid shows the same field order as the main list — Pending actions and remarks right after Project scope, Project status at the end — and the same Show/Hide Columns control works on it too.

CHAPTER 4

The Team Allocation tab

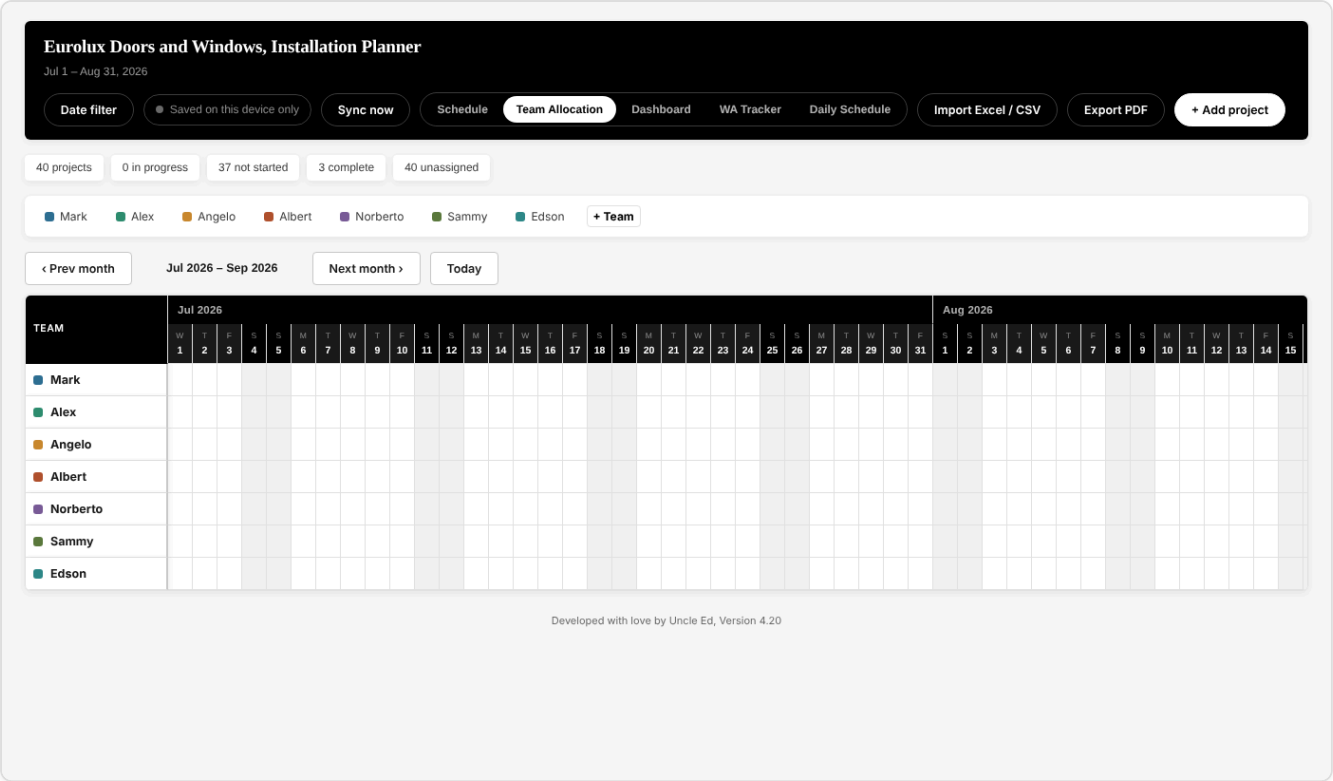


Team Allocation — who's on which job, month by month.

A month-by-month view, one row per team, with each project shown as a bar across the days it's scheduled. Overlapping bars on the same team's row flag a conflict — two projects booked for the same team on the same day — so double-bookings are easy to spot before they become a problem on site. Use the arrows to move between months, or **Today** to jump back to the current one.

CHAPTER 5

The Dashboard tab

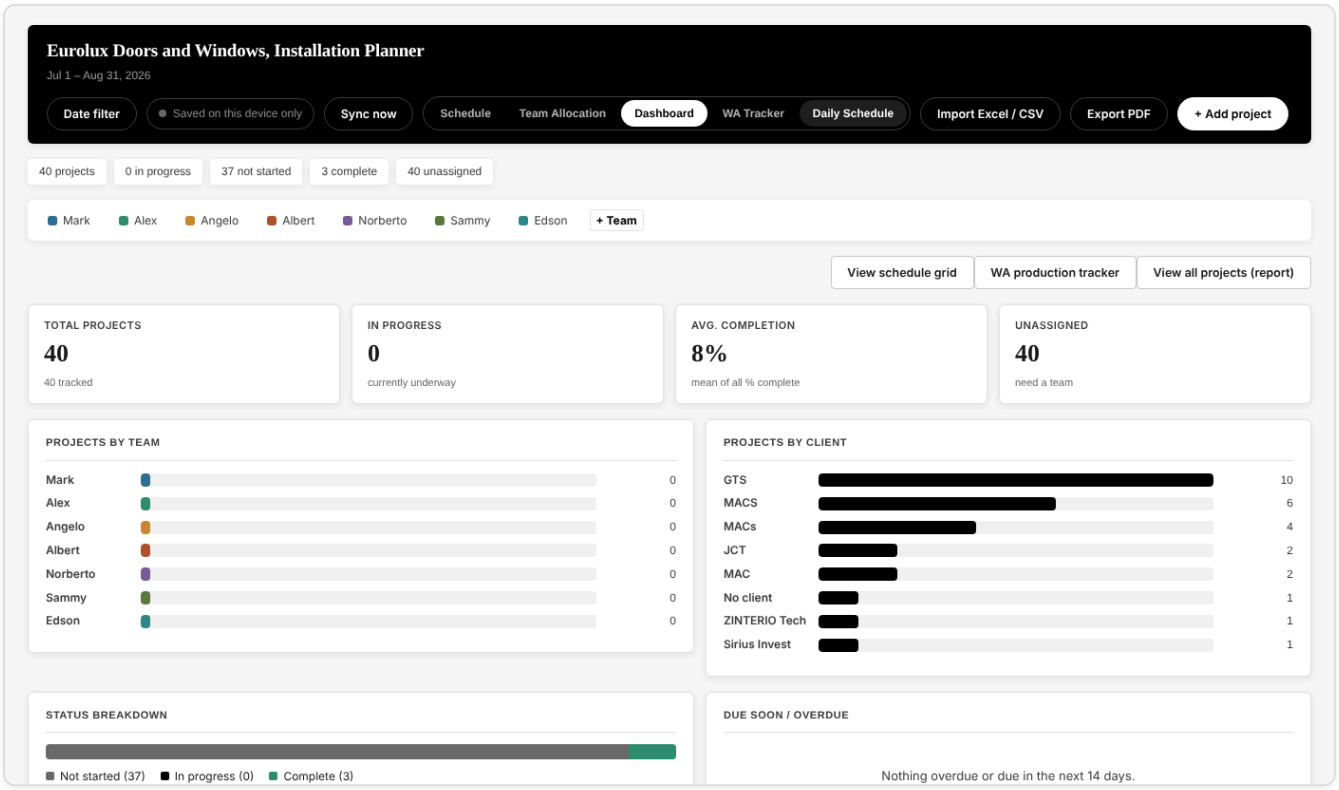


The Dashboard — KPI cards, charts, and the Settings panel.

KPI cards (total projects, in progress, average completion, unassigned), a projects-by-team chart and a projects-by-client chart, a status breakdown bar, and a due-soon/overdue list. **View schedule grid** and **WA production tracker** jump straight to those screens; **View all projects (report)** opens a clean, printable table of everything. The Settings panel (inside this tab) is also where **Clear all** lives, for wiping the schedule and starting fresh — see Chapter 10 for the safety net around that.

CHAPTER 6

The WA Tracker tab

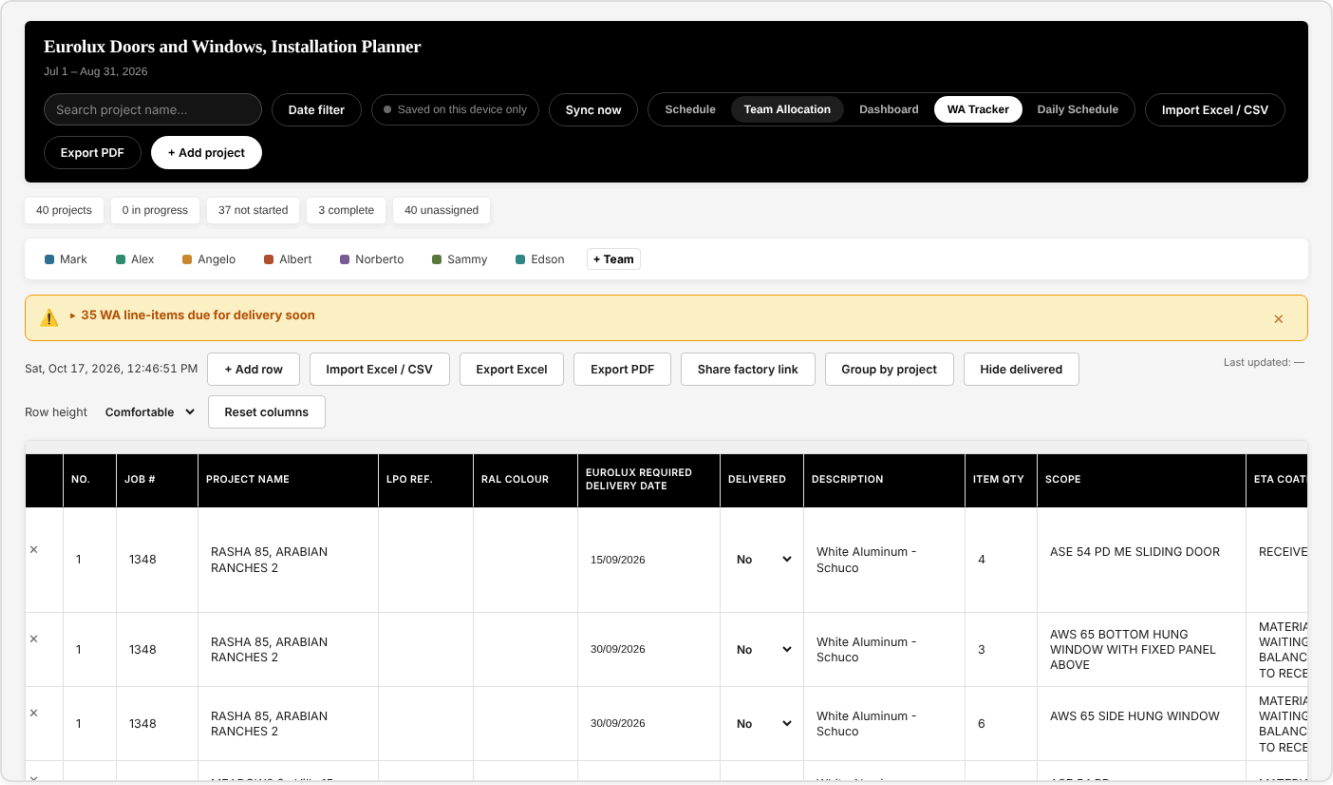

The WA production tracker — glass, frame and coating status per line-item.

A second, separate board for glass/frame/coating fabrication status — its own full-screen tab, not a popup. It tracks No., Job #, Project Name, LPO Ref., RAL Colour, Eurolux Required Delivery Date, Delivered Yes/No, Description, Item Qty, Scope, ETA Coating, ETA Fabrication Frame, ETA Fabrication Shutter, and Remarks.

Use **+ Add row** for a blank line-item, the × on the left of each row to delete one, and **Import Excel / CSV** to bring in a tracker-shaped sheet. Setting **Delivered** to **Yes** turns the whole row green so delivered items stand out while scanning a long list. **Group by project** clusters line-items that share a Project Name under a collapsible header; **Hide delivered** hides everything already marked Delivered.

> **New:** the WA Tracker's own search box is gone — it now shares the one search field in the main toolbar (see Chapter 1). Switch to this tab and the same box filters WA Tracker rows instead of Schedule projects.

A delivery-due banner (amber, collapsed to a one-line summary) appears automatically whenever a not-yet-Delivered row is due within 7 days or overdue. A separate field-updated banner highlights anything edited in the last 24 hours. Both are dismissible for your current visit and come back the next time something qualifies.


CHAPTER 7

Sharing the WA Tracker with the factory

Click **Share factory link** in the WA Tracker toolbar to copy a link to `wa-tracker.html` — a standalone page that shows and edits only the production tracker, nothing else from the planner. It's the same live data (same backend), just without the Schedule, Dashboard, Team Allocation, or Daily Schedule tabs, so it's safe to hand to the factory without giving them visibility into client/project details elsewhere in the app.

CHAPTER 8

The Daily Schedule tab

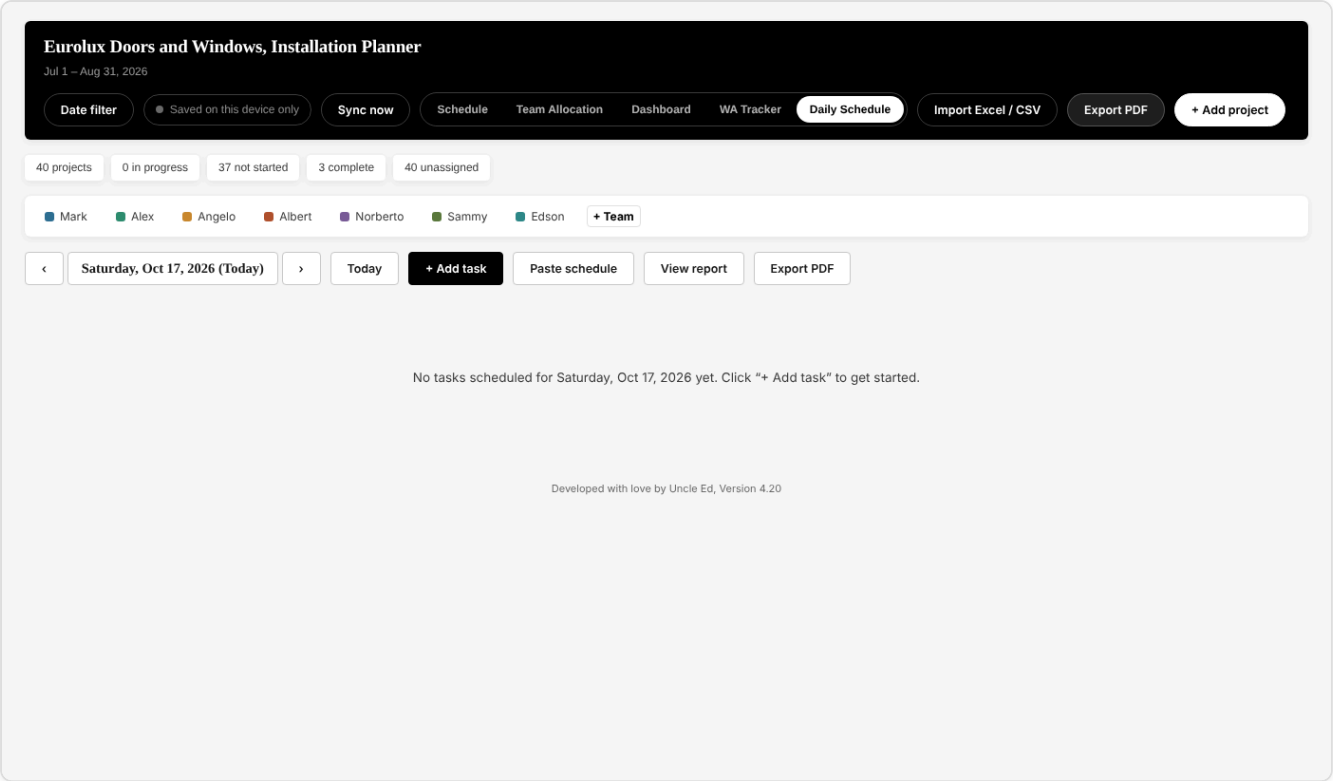

Daily Schedule — replaces the morning WhatsApp message.

Instead of typing up "Mark's Team: … / Albert's Team: …" and sending it to the group chat every morning, the plan now lives in its own tab that everyone sharing the planner sees live. Date arrows and **Today** move between days — every day's plan is kept, so you can page back through history.

+ Add task creates a blank task; pick a **Team**, type the **Project / location** (autocompletes against your project list) and the task, with an optional **Comments** field. Tasks group into a card per team. Use **+ Support teams** to tag one or more additional teams helping on the same task.

Paste schedule turns a WhatsApp-style message straight into tasks — paste the whole message and it parses as you type, including a "with <Name>'s Team" support-team mention and any date mentioned in the text. A live preview shows exactly what's about to be created, with any new team name flagged, before you click **Add tasks**. **View report** gives a clean read-only summary of the day; **Export PDF** saves it as a landscape PDF.

CHAPTER 9

How the installation process maps to the app

This chapter ties the app's fields to how the office actually runs a job, for anyone new to the process.

1. **Design approved.** The order goes to two different suppliers: the door/window supplier, and — separately — a glass manufacturer. These are tracked as **Frame delivery date** and **Glass delivery date**.
2. **Manufacturing.** Frames typically take 6–8 weeks; glass takes 2–4 weeks. Some glass ships straight to site; otherwise it goes to the frame supplier first to be bonded (see the **Bonding required** field), then both are collected together.
3. **Collection and delivery.** Once ready, the supplier notifies the office, who arrange collection and delivery to site.
4. **NOC and access pass.** Every site needs one, normally applied for about a week before installation. A typical install takes a week; large projects can run 3–4 weeks — log progress in **% complete** and day-to-day work on the **Daily Schedule** tab.
5. **Delivery payment.** Once items are ready, Accounts requests the delivery payment from the client. **Installation cannot start until that payment is confirmed** — note the payment status in **Pending actions and remarks** if it's holding up the start date.
6. **Snagging.** After installation, a snagging inspection catches anything needing fixing or calibrating before handover.
7. **Handover.** Once snagging items are closed out, the project is handed over to the client.

The **Project status** dropdown (Chapter 2) is how that whole lifecycle — Installation in progress → Snagging in progress → Snagging completed → Awaiting handover to client → Handed over, or simply Completed — is tracked on each project row, alongside the dated notes in Pending actions and remarks for anything that doesn't fit a single field (a payment that's outstanding, an access pass delay, a snag that needs a supplier visit, and so on).

CHAPTER 10

Tips, safety nets and troubleshooting

Undo

Deleting a project, a WA Tracker row, or a Daily Schedule task — and importing a batch of either — shows a brief **Undo** option before the change is final. Anything bulk (an import, a pasted schedule) undoes as a single step, not one row at a time.

Clear all

Found in the Dashboard's Settings panel — wipes the Schedule back to empty. This is for starting completely fresh; it asks for confirmation first and is not something you'd use day to day.

Installing the app

The planner is an installable PWA — look for "Install App" or "Add to Home Screen" in your browser's menu to get it as its own app icon, with basic offline support (you can keep viewing and editing; changes sync once you're back online).

Per-device settings

Column widths, hidden columns, Compact/Normal view, Show hidden rows, and WA Tracker grouping are all remembered per device, not synced — what you set up on the office computer won't change how it looks on someone else's screen or the factory tablet. The actual project data (everything in the Schedule, WA Tracker, and Daily Schedule) is the one thing that *does* sync, whenever "Synced with team" is showing.

Where the data lives

The shared data lives in Firestore, a schemaless cloud database — there's no SQL database involved anywhere in this app, and no database schema to migrate when a field like Project status is added: the app fills in a sensible default for every project the first time it loads one that's missing a newer field. Nothing about adding Project status, moving Pending actions, or any of the other changes in this edition required changing anything on the backend.
